

Project Plan

GlamUp! Online Beauty Services App

Primary Instructor	Anjana Shah
Team Member	Kashfi Mehbuba
Team Member	Melissa Paksoy
Team Member	Meric Yassine

Document Revision History

Revision #	Date
1.0	06/10/2025
1.1	07/10/2025
2.0	05/02/2026
2.1	08/02/2026

Table of Contents

1. Executive Summary	3
2. Project Approvers, Reviews and Distribution List	3
3. Scope	4
4. Deliverables	5
5. Assumptions	6
6. Dependencies	7
7. Risk Management	8
8. Communication	9
9. Task Listing	10
10. Gantt Chart	11
11. Milestones	11
12. RAM	12
13. Approval	12

1. Executive Summary

The following describes the project to be executed:

Objective	The objective of the GlamUp project is to design and develop an application that connects clients with freelance nail technicians, lash artists, and makeup professionals in a convenient, accessible, and user-friendly way. The app will allow customers to browse professional profiles, compare services and prices, view availability, and book appointments seamlessly. At the same time, it will provide professionals with a platform to showcase their work, manage bookings, and grow their clientele. By combining convenience for customers with visibility for beauty professionals, GlamUp aims to modernize and simplify the process of accessing personalized beauty services. The GlamUp application will be developed as a mobile-only solution using React Native to ensure compatibility across both Android and iOS platforms.
Corporate Goals Addressed	N/A
Planned Start Date	Monday, September 8, 2025
Planned End Date	Thursday, April 2, 2026
Note	This project plan was revised in Winter 2026 to reflect changes in team composition and updated project responsibilities.

2. Project Approvers, Reviews and Distribution List

Approvers, reviewers and distribution list:

Project Role	Name	Date
Instructor	Anjana Shah	TBD
Team Member	Kashfi Mehbuba	08/02/2026
Team Member	Melissa Paksoy	08/02/2026
Team Member	Meric Yassine	08/02/2026

3. Scope

This section defines the scope of the GlamUp! project by outlining all features, functionalities, and requirements that are included in the application, as well as those that are explicitly excluded from the project deliverables.

In Scope	Out of Scope
1. <u>User Accounts & Profiles</u> - Customers can create and manage accounts. - Beauty professionals can create business profiles with portfolios, pricing, and availability.	1. <u>Advanced Customer Support:</u> Features such as integrated live chat, 24/7 support agents, or AI chatbots are excluded.
2. <u>Service Discovery</u> - Customers can browse and compare professionals based on services, prices, reviews, and ratings. - Search and filter functionality for beauty service categories.	2. <u>Marketing and Promotions Tools</u> Loyalty programs, promotional codes, referral systems, or in-app advertisements are not part of this project.
3. <u>Professional Profile</u> - Professionals can showcase their work with sample photos. - Customers can leave reviews and ratings.	3. <u>AI-driven Recommendations</u> Personalized recommendations based on user preferences, reviews, or past bookings will not be developed at this stage.
4. <u>Appointment Booking</u> - Customers can view availability and book appointments directly in the app. - Time-slot selection for convenient scheduling.	
5. <u>Basic Communication</u> Booking confirmation notifications within the app.	

4. Deliverables

This project will deliver the following:

Deliverable	Description
A mobile application	A functional mobile application built using React Native, compatible with both Android and iOS platforms, allows customers to browse professionals, view services, and book appointments. It includes core features such as user profiles, service discovery, booking management, reviews, availability, and a booking confirmation flow.
Project Documentation	The project documentation includes the Project Vision, High Levels Requirement document, Project Plan, User Personas & Stories, Team Charter, Product Backlog and Sprint Backlog.
Registration/Login System	Customers can to create and manage accounts. Beauty professionals can create business profiles with portfolios, pricing, and availability. Staff can log into their administrative accounts in order to monitor and handle user feedback and conflicts.
Search & Filter Component	Customers can browse and compare professionals based on services, prices, reviews, and ratings, using the search and filter functionality for beauty service categories.
Booking Flow Prototype	A demonstrable booking process includes selecting services, choosing a date/time, and confirming a booking.
Ratings & Reviews System	Customers can leave ratings and reviews on beauty professionals based on their experience, and view feedback left by other customers to make the best decision. Admins can monitor the reviews and take actions accordingly.
Professional Profiles & Dummy Data	Sample professional listings with mock services, pricing, availability slots, and gallery images demonstrate app functionality. This allows realistic testing of the booking process without relying on live data.
Basic Communication Feature	Customers and beauty professionals can send direct messages to each other to ensure seamless and time-efficient communication

5. Assumptions

This project makes the following assumptions:

User Access	Customers and professionals will have access to Android or iOS smartphones with stable internet connectivity
Data Availability	All professional and service data (e.g., prices, availability, photos) used in the prototype will be preloaded or simulated with dummy data.
Backend Services	A simplified backend will be sufficient for storing and retrieving user, service, and booking data during development
Development Tools	Visual Studio Code, React Native tooling and GitHub will remain the main development and version control platforms throughout the project.
Team Collaboration	All project contributors will have consistent communication and shared access to the repository and documents
Testing Scope	Application testing will focus on functionality and user interface flow, not on performance or scalability under real-world loads.

6. Dependencies

The following are the internal and external dependencies that will have to be acknowledged and addressed:

Internal Dependencies

1. **Team Collaboration and Coordination**: The project's progress depends on consistent communication, timely code commits, and proper version control through GitHub.
2. **UI/UX Design Completion**: The development of the app's core screens depends on the completion and approval of the wireframes and design layouts.
3. **Backend and Frontend Integration**: The booking and profile features rely on proper synchronization between the backend data and the frontend interface.
4. **Testing & Debugging**: Timely identification and resolution of bugs depend on the availability and collaboration of all team members during the testing phase.

External Dependencies

1. **Development Environment**: The project depends on stable React Native development tooling and operating systems (Android and iOS).
2. **Firestore or Database Services**: The availability and reliability of cloud or database services (e.g., Firestore) are required for data storage and retrieval.
3. **Internet Connectivity**: Continuous internet access is needed for real-time data fetching, authentication, and syncing with remote databases.
4. **Device Compatibility**: The application depends on supported Android and iOS versions that meet minimum performance and layout requirements.

7. Risk Management

Potential Risk	Severity (H/M/L)	Likelihood (H/M/L)	Management Strategy
Technical Integration Issues (frontend and backend not syncing correctly)	H	M	Conduct early integration testing; maintain clear API/data model documentation; schedule regular code reviews.
Data Loss or Corruption during development	H	L	Use GitHub for version control and maintain regular backups of project files and Firebase data.
Team Communication Gaps causing delays or misalignment	M	M	Hold regular team meetings, use shared communication tools (e.g., Slack, Teams), and assign clear task ownership.
Limited Testing Time leading to undetected bugs	H	H	Begin testing early in the development cycle; assign dedicated time for debugging before submission.
Tool or Software Issues (Visual Studio Code, Firebase outages)	M	L	Keep tools updated, maintain local backups, and have contingency plans for temporary offline development.
Scope Creep (adding new features late in the project)	M	M	Freeze the feature list after the scope approval; document any future enhancements as “Phase 2.”
Device Compatibility Problems (UI not displaying properly on different Android and iOS devices)	H	L	Test the app on multiple screen sizes and Android/iOS versions; use responsive layouts.
Dependency on Internet Connection (for Firebase and online data access)	M	M	Provide local caching or placeholder data for testing when offline; ensure stable connections during demos.

8. Communication

Reporting

The following reports will be produced;

Report	Audience	Frequency
Progress Report	Team Members + Instructor	Weekly
Team Development Update	Team Members	Twice a week
Issue & Risk	Team Members	As needed

Meetings

The following meetings/communication will be established;

Meeting	Purpose	Attendees	Frequency
Team Stand-up Meeting	Discuss progress, assign tasks, and identify blockers	Team Members	Weekly
Technical Collaboration Session	Resolve integration or coding issues, review pull requests, and test features	Team Members	As needed
Design Review Meeting	Review UI/UX design updates, wireframes, and flow consistency	Team Members	Bi-weekly

9. Task Listing (WBS- Work Breakdown Structure)


The Work Breakdown Structure (WBS) outlines the major phases and tasks required to complete the GlamUp project, including their estimated durations and dependencies, to support effective scheduling and project control.

Reference	Tasks	Duration	Dependency
1.0	Project Initiation & Planning	3 weeks	None
1.1	Define project objectives, scope, and deliverables	2 weeks	None
1.2	Assign roles and responsibilities within the team	3 days	1.1
1.3	Set up GitHub repository and folder structure	1 week	1.2
2.0	Design Phase	8 weeks	1.0
2.1	Develop user personas and user stories	1 week	1.0
2.2	Create wireframes and UI flow diagrams	5 weeks	2.1
2.3	Review and finalize UI/UX design	2 weeks	2.2
3.0	Development Phase	12 weeks	2.0
3.1	Set up project	5 days	2.3
3.2	Develop Core Application Pages	7 weeks	3.1
3.3	Implement Booking functionality and data simulation	3 weeks	3.2
3.4	Integrate database with mock data	5 days	3.3
3.5	Conduct frontend-backend integration testing	4 days	3.4
4.0	Testing & Refinement	2 weeks	3.0
4.1	Functional testing (UI navigation, booking flow)	4 days	3.6
4.2	Debugging and fixing issues	5 days	4.1
4.3	Usability testing and adjustments	5 days	4.2
5.0	Documentation & Presentation	3 weeks	4.0
5.1	Compile project documentation	5 days	None
5.2	Prepare final presentation and demonstration	2 weeks	5.1
5.3	Final review and submission	2 days	5.2

10. Gantt Chart

GlamUp! Online Beauty Services

Gantt Chart (Sep 8, 2025 - Apr 2, 2026)

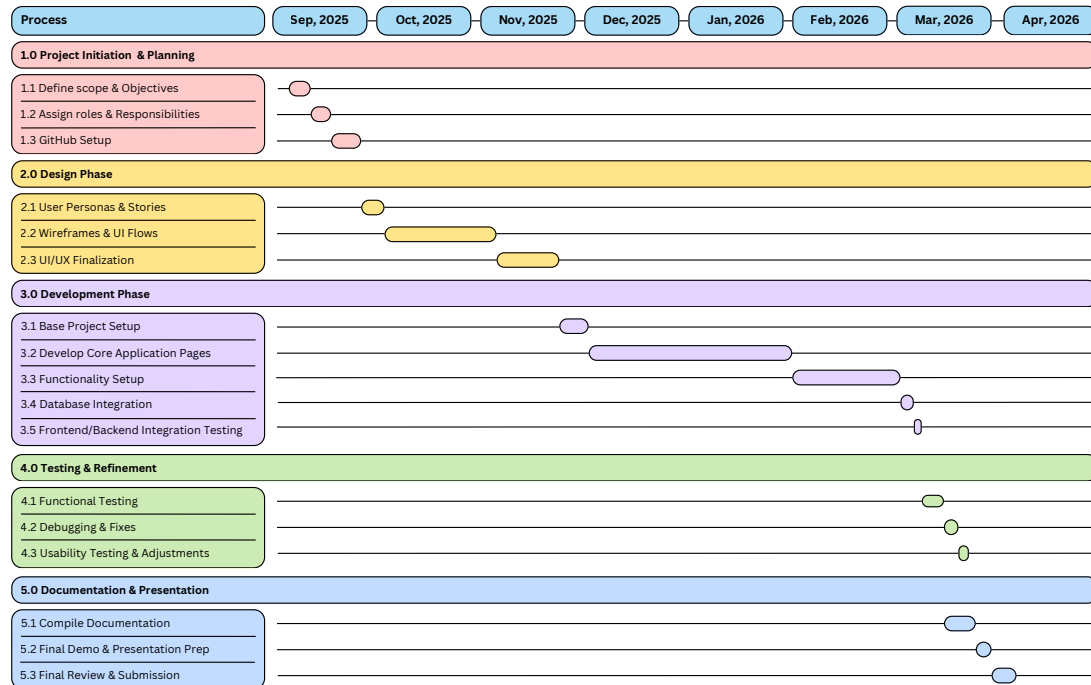

11. Milestones

Major Activity or Milestone	Estimated Milestone Target date	Owner/Reviewer Team Members
Project Initiation & Planning Completed	Sep 26, 2025	Team Members + Instructor
Design Phase Completed (Wireframes & UI Finalized)	Nov 22, 2025	Team Members
Core App Structure Setup Completed (Navigation & Base Screens)	Jan 18, 2026	Team Members
Core App Pages & Functionality Completed	Mar 1, 2026	Team Members
Backend Integration Completed (Firebase / Mock Data)	Mar 10, 2026	Team Members
Testing & Refinement Completed	Mar 24, 2026	Team Members
Documentation & Presentation Finalized	Mar 29, 2026	Team Members
Final App Demonstration & Submission	Apr 2, 2026	Team Members

12. RAM – Responsibility Assignment Matrix

Responsibility Assignment Matrix (RAM)

Legend:

A/R: Accountable/Responsible R: Responsible I: Informed C: Consulted

Task/Phase	Kashfi Mehbuba	Melissa Paksoy	Meric Yassine
Project Planning	A/R	C	C
User Personas & Stories	A/R	I	R
Design Phase (Wireframes)	A/R	R	R
Development Phase (Functionality)	A/R	R	R
Testing & Debugging	A/R	R	C
Documentation & Presentation	A/R	C	C

13. Approval

The signatures below indicate their approval of the contents of this document.

Project Role	Name	Signature	Date
Team Member	Kashfi Mehbuba	kashfi.mehbuba@georgebrown.ca	08/02/2026
Team Member	Melissa Paksoy	sevim.paksoy@georgebrown.ca	08/02/2026
Team Member	Meric Yassine	meric.yassine@georgebrown.ca	08/02/2026
